


Health, Safety & Environmental

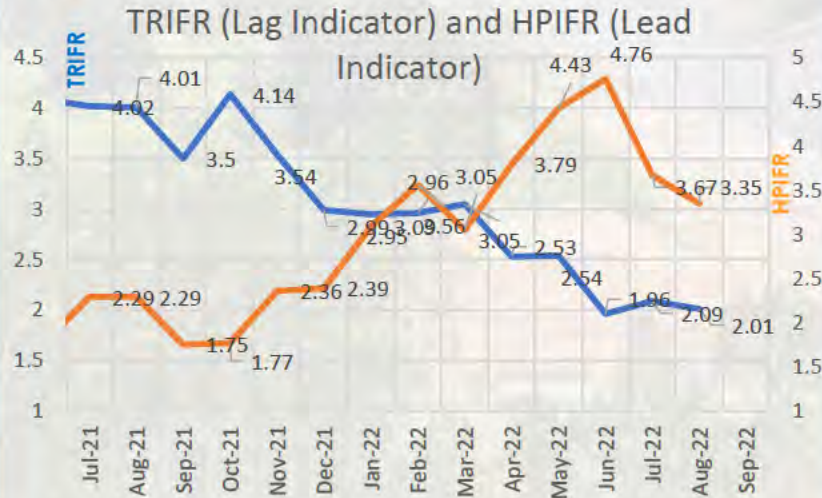

Observed and emerging Issues


- **One RTA** in the period – head on collision on Waiwera viaduct under contraflow TTM operations.
- **Critical risk (CR) inspection** targets met for Oct (27), high CR focus important as project nears completion.
- **No environmental performance** concerns raised on 25 October audit, AC did note increase in EW activity.

ESC Inspection Scores				
Date	1	2	3	4
25 Oct (south)	26	10	-	-
25 Oct (north)	19	8	-	-

Progress vs Programme

Project progress | Status | Trend

Site Monitor measured progress is ahead of the BL09 baseline programme by 1.3% or 13 weeks.

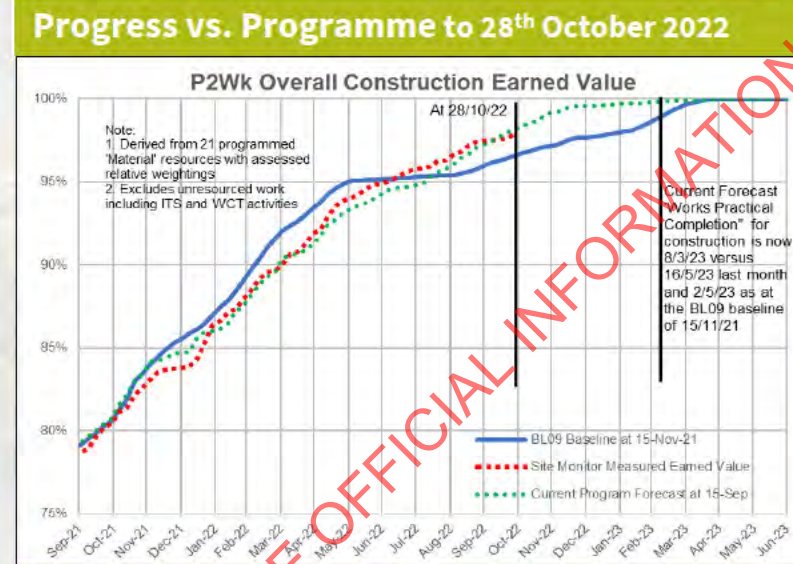

Key Progress & Notable Delays since 1st October

- Most **activities** reported in the previous dashboard have continued with steady progress throughout the period.
- **Subgrade preparation and pavement construction** continuing on south bound lanes between the northern roundabout and MLRi.
- **WM5** pond and slip earthworks continuing.
- Works continue to **Perry Rd access track**.
- **OGPA** surfacing between SAP3 and Northern RBT.
- **Slip remediation** earthworks continues across the project – **CN12, CS5, CS16D and Mahurangi Access**. Additional **slope remediation** occurring at **CS5**.
- **Shotcreting to pavement shoulder** ongoing.
- **Median Drains** are almost complete site wide, minor finishing to do.

S	S	M	T	W	T	F
15	16	17	18	19	20	21
22	23	24	25	26	27	28

RELEASED UNDER THE OFFICIAL INFORMATION ACT 1982










s 9(2)(j)

s 9(2)(j)

s 9(2)(g)(i)

CONSTRUCTION GRAPHS

Progress vs Programme Note: Baseline is BL09 of 15/11/21

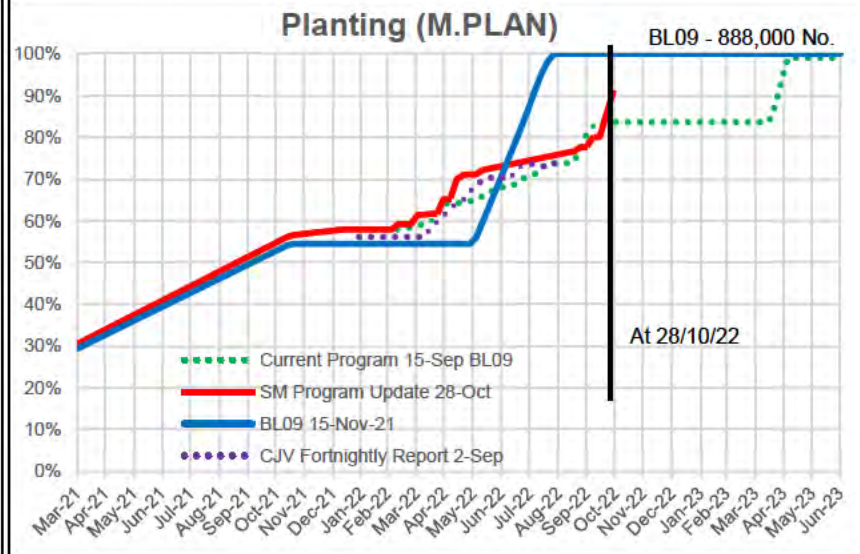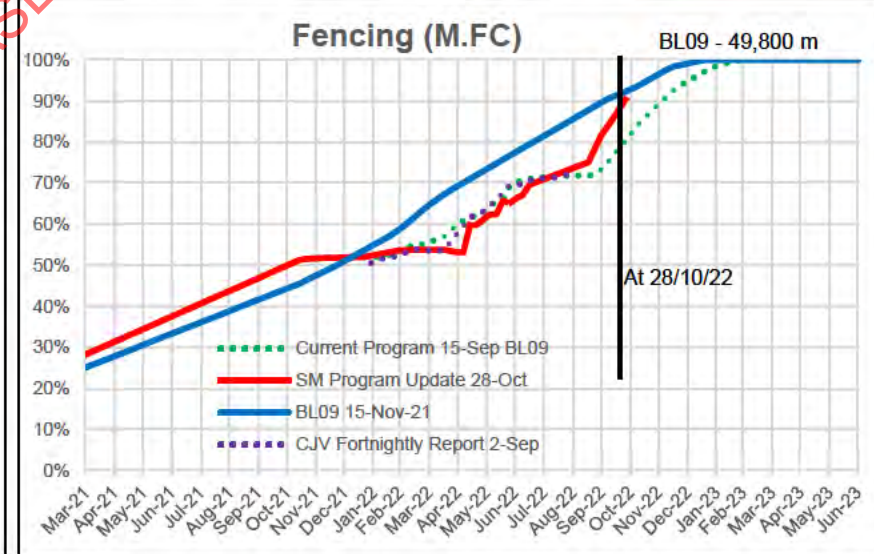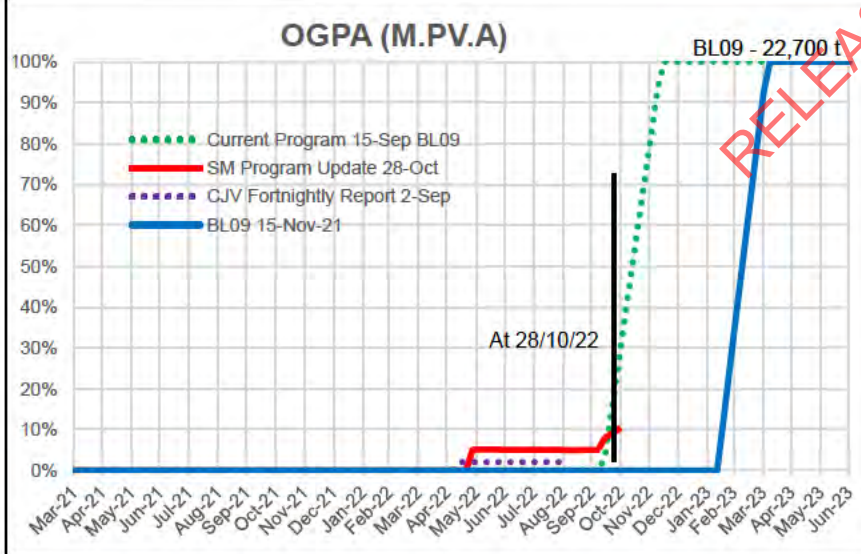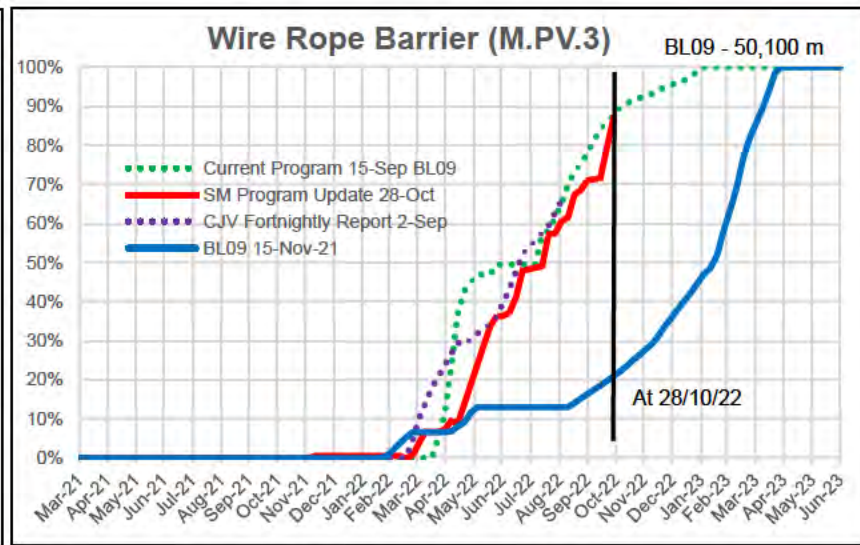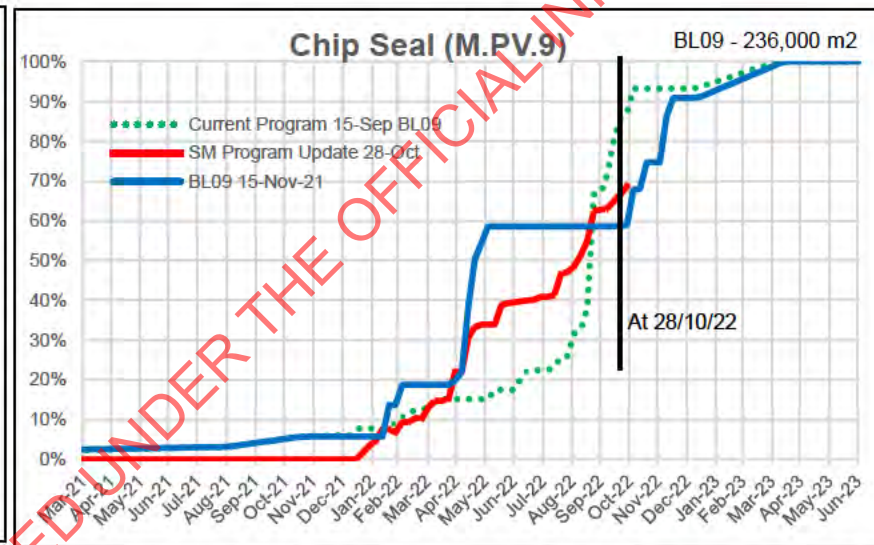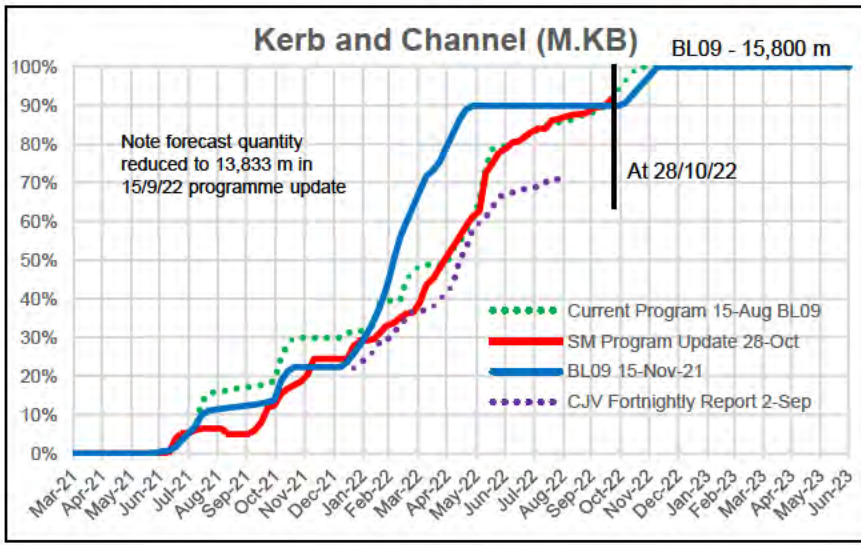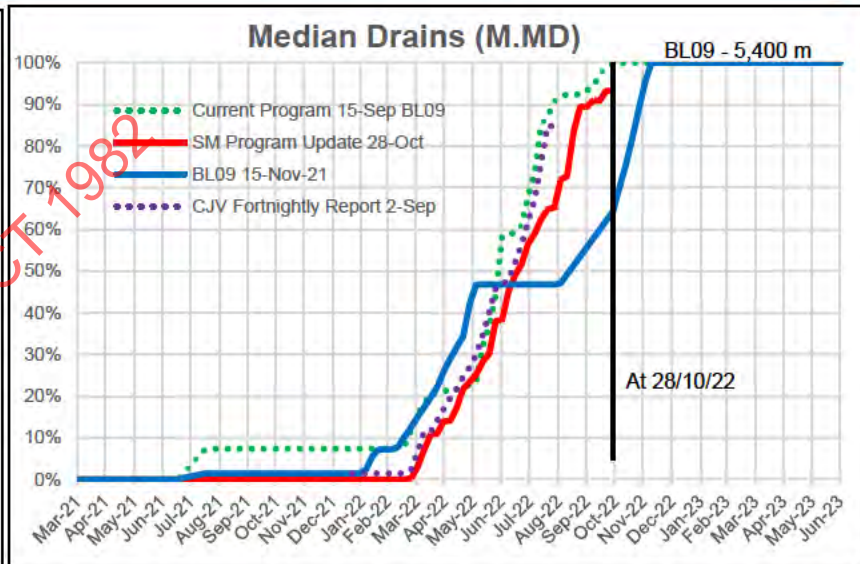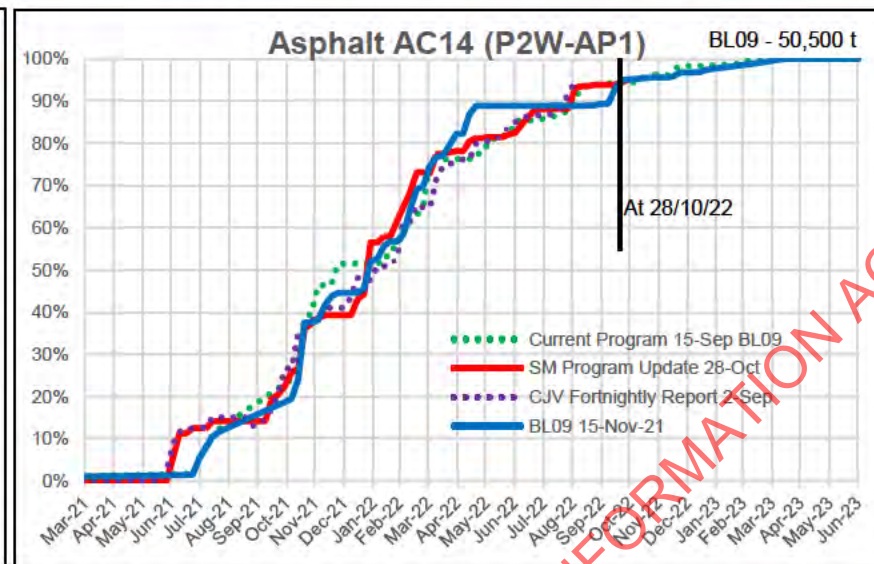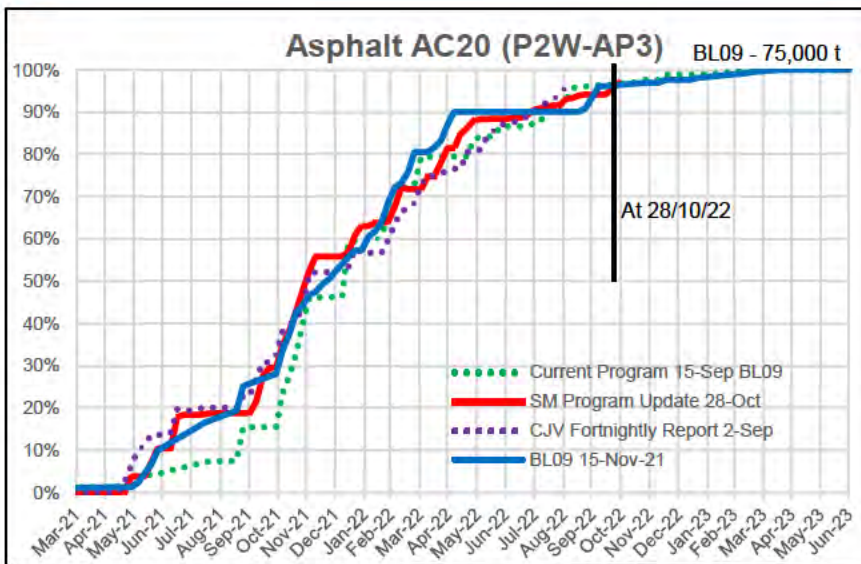

RELEASED UNDER THE OFFICIAL INFORMATION ACT 1982

RELEASED UNDER THE OFFICIAL INFORMATION ACT 1982

PROGRESS PHOTOS

27/10/22 Pavement Construction Western Leg by Goatley Rd (SB)



26/10/22 Pavement Construction at MRLi (towards SH1)



27/10/22 WM5 Lime stabilisation of permanent pond



25/10/22 Large earthworks/shaping around Brokeback (looking SB)



PROGRESS PHOTOS

25/10/22 Swale cleanout for upcoming ShotCreting at CN7 (looking SB)



28/10/22 Additional slope stabilisation at CS5 inc counterfort drains (Eastern side)



27/10/22 Cast insitu concrete barrier transition at Puhoi Bridge



28/10/22 Soil Nail installation nearing completion at Okahu Viaduct (looking Northbound)



DASHBOARD

Plan showing P2Wk Alignment

