


**Health, Safety & Environmental**

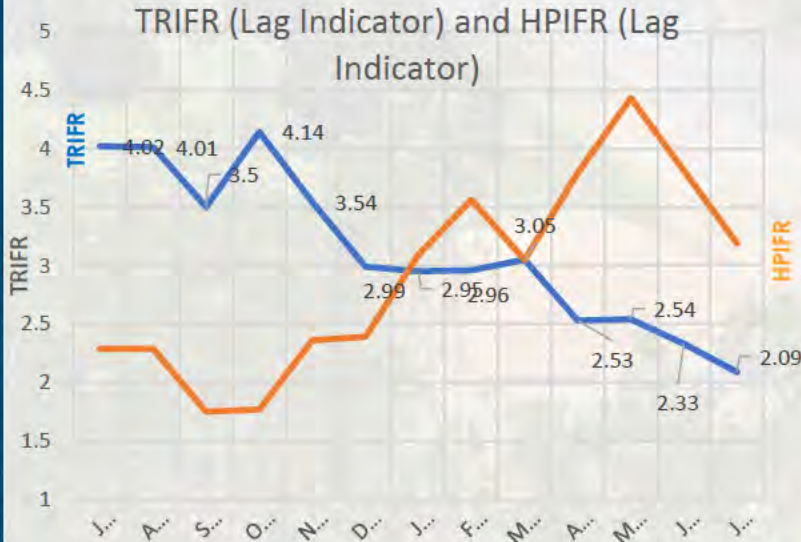


**Observed and emerging Issues**

- No recordable safety incidents reported in the period.
- Critical risk inspection targets generally being met.
- Environmental audit scores for inspection on 2<sup>nd</sup> August not yet available. Comments from Auckland Council Inspector on 2<sup>nd</sup> Auckland reflect continued good environmental performance.

**Progress vs Programme**

Project progress	Status	Trend
Rate of overall progress tracking about <b>56 working days ahead of BL09 baseline dated 15/11/21.</b>		




**Progress vs. Programme to 5<sup>th</sup> August 2022**

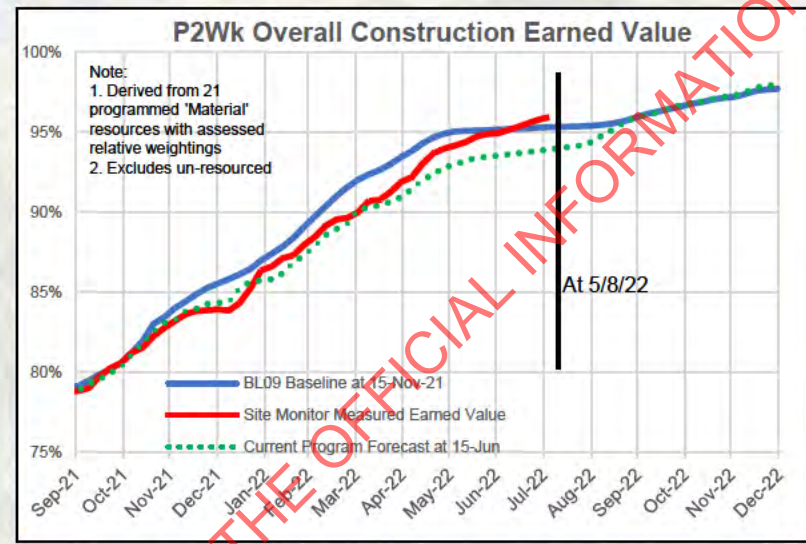

**Key Progress & Notable Delays since 22<sup>nd</sup> July**

- **Watson Road south abutment and RECO walls reconstructed. Backfill** under way.
- **N3C Engineered slope.** Slipped material has been removed and backfilled with GAP65 under way.
- **Some topsoil slips** spread with hay and hydroseeded.
- **AP40 stage 1 at Northern Connection roundabout** close to completion. **AC20 asphalt** being laid.
- Continued good progress on **median drains**.
- Slow progress at **Southern Connection** as Art Work plinths completed.
- **Site workforce** of **114** recorded on 4/8/22, a slight increase from 112 the week before.
- Weather impacts on **4 working days** in the period.










S	S	M	T	W	T	F
23	24	25	26	27	28	29
30	31	01	02	03	04	05



RELEASED UNDER THE OFFICIAL INFORMATION ACT 1982

# DASHBOARD GRAPHS




Progress vs Programme Note: Baseline is BL09 of 15/11/21

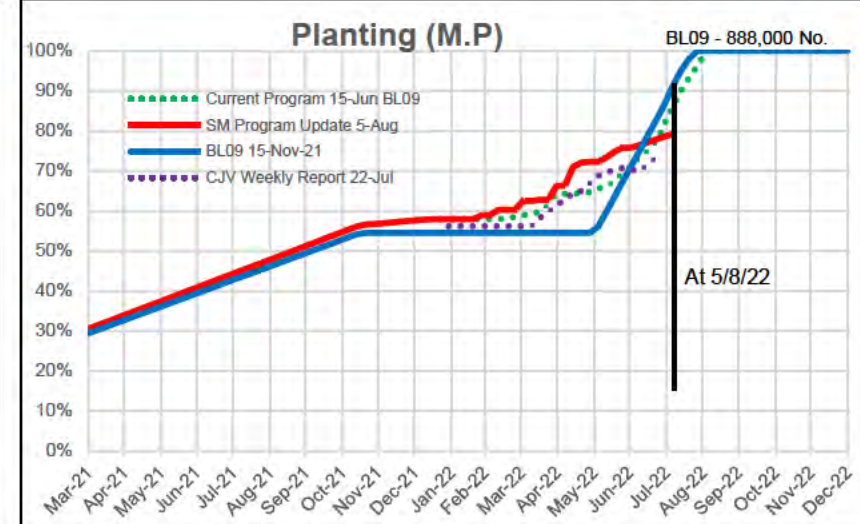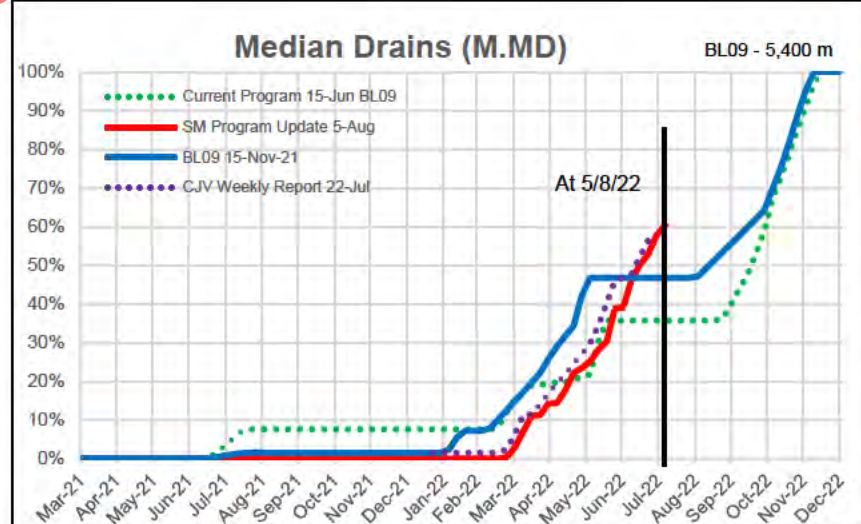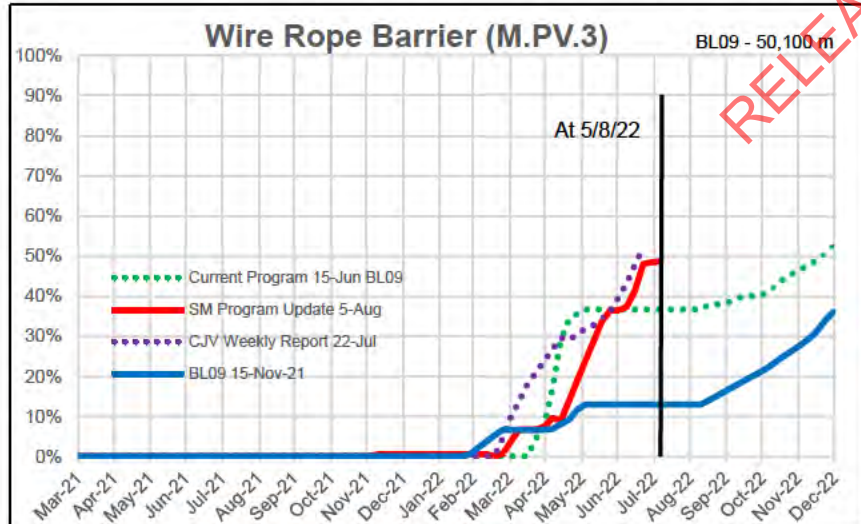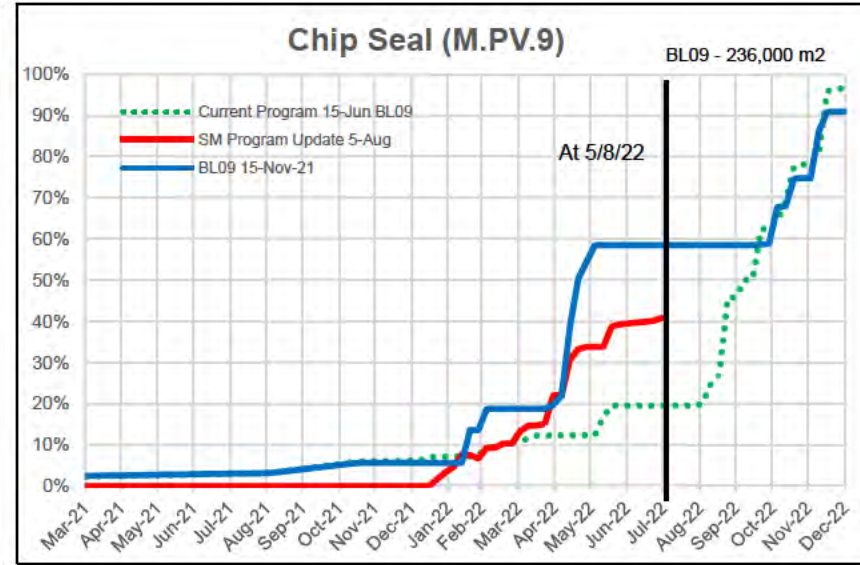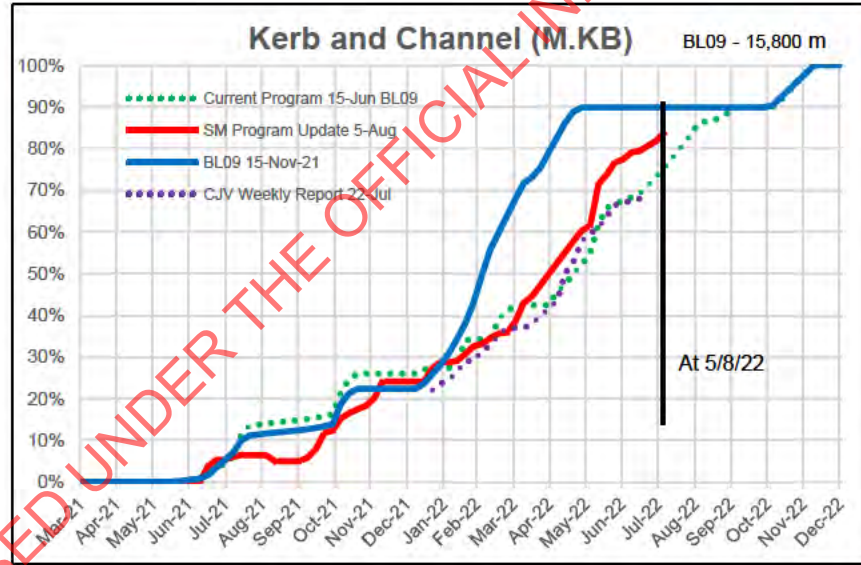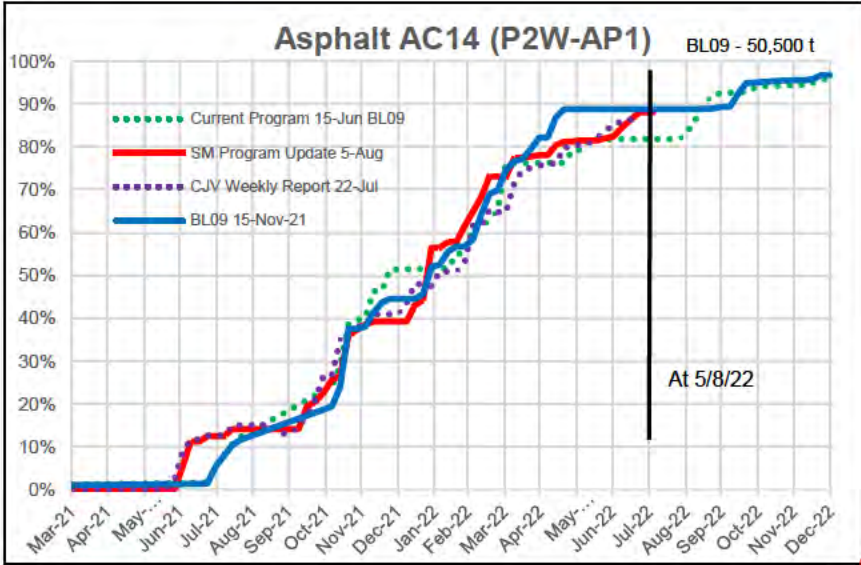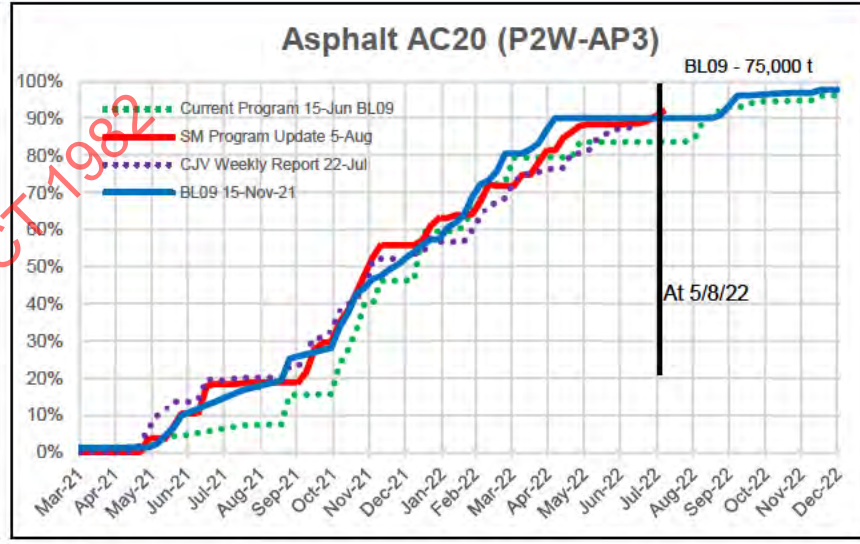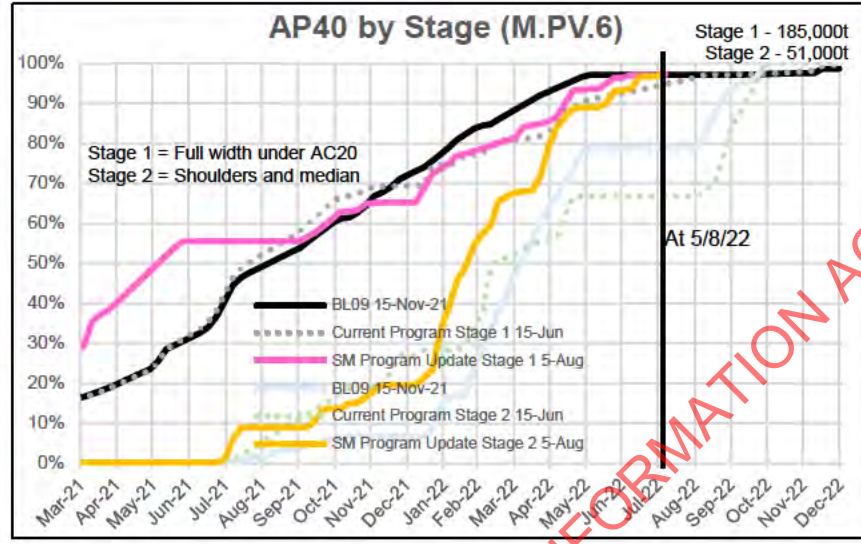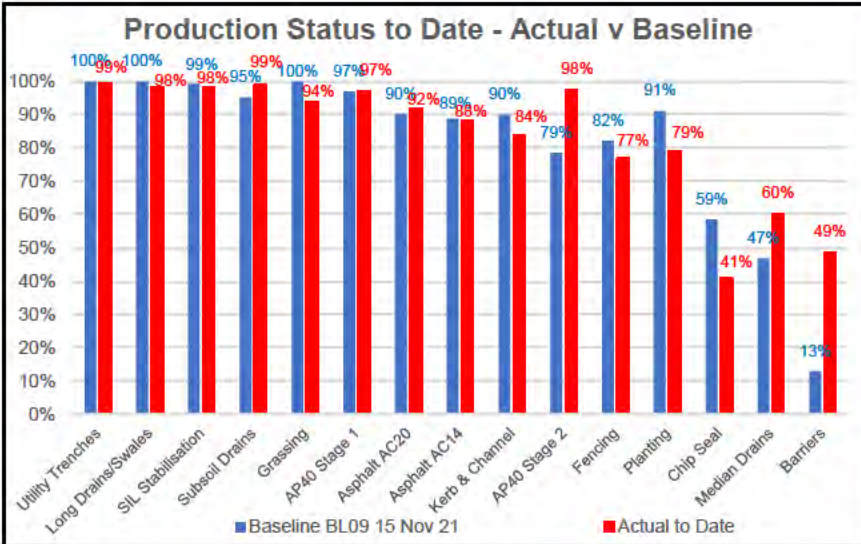

RELEASED UNDER THE OFFICIAL INFORMATION ACT 1982

# DASHBOARD GRAPHS

Progress vs Programme Note: Baseline is BL09 of 15/11/21

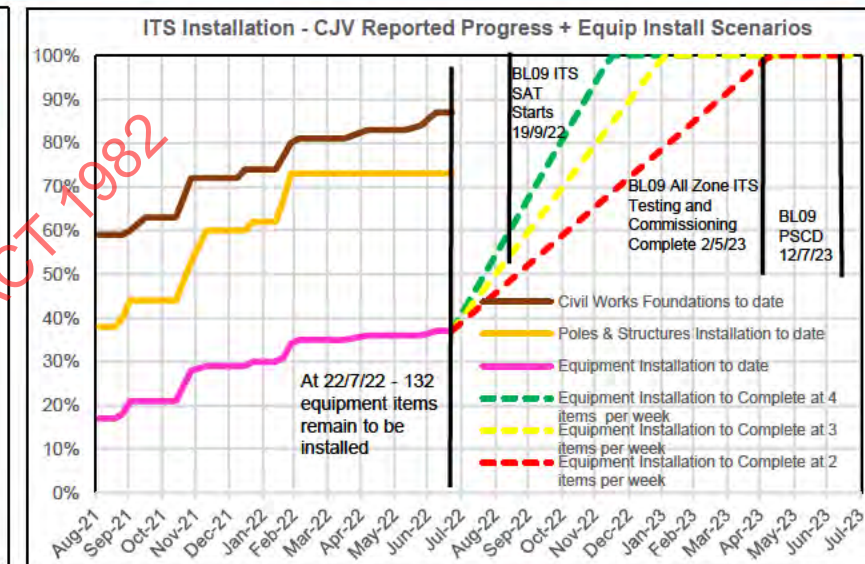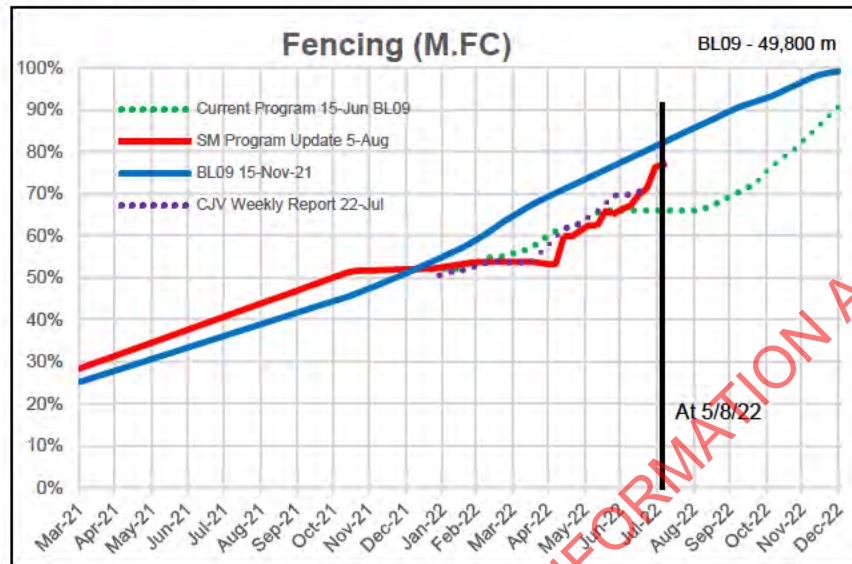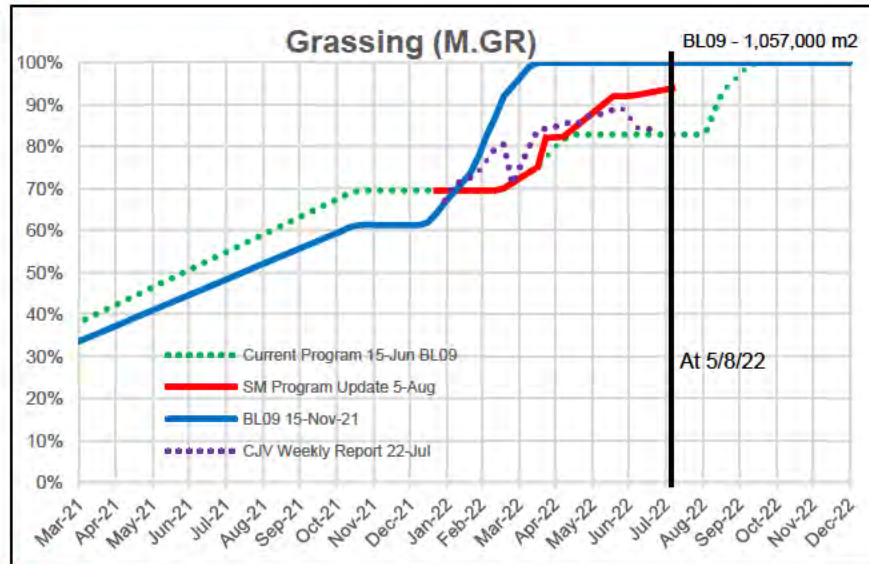

s 9(2)(j)

RELEASED UNDER THE OFFICIAL INFORMATION ACT 1982

# FORTNIGHTLY DASHBOARD

Progress Photographs

2/8/22 Slip next to Mahurangi Logging Track



5/8/22 Watson Road Bridge Reconstructing RECO walls and straps



5/8/22 Northern Connection. Reconstructed SH1 northbound



5/8/22 CS2 ch 57500 Prime/chipseal on southbound shoulder



# INTERIM DASHBOARD

Progress Photographs

5/8/22 Plinths for Art Work at Southern Connection



29/7/22 Filling Slip at N3C with GAP65



5/8/22 Matakana Link Road Intersection



29/7/22 Installing Median Drains CN5



