


Health, Safety & Environmental

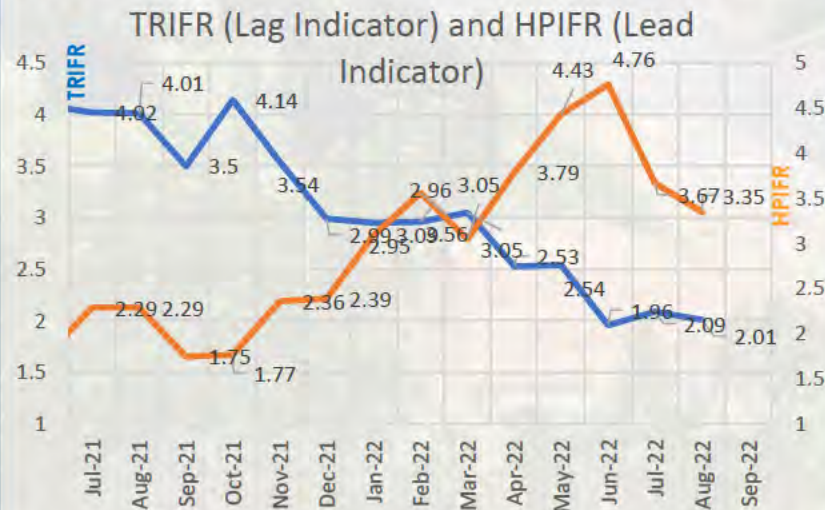

Observed and emerging Issues


- **No recordable safety incidents** reported in the period.
- **Critical risk inspection targets for September** already exceeded.
- **Good environmental performance** continues to be reflected in AC inspection on 13 September.

ESC Inspection Scores				
Date	1	2	3	4
13 Sept (south)	35	2	-	-
13 Sept (north)	31	2	-	-

Progress vs Programme

Project progress	Status	Trend
Site Monitor measured progress is ahead of the latest programme revision by 1.3%.		➔




Progress vs. Programme to 16th September 2022

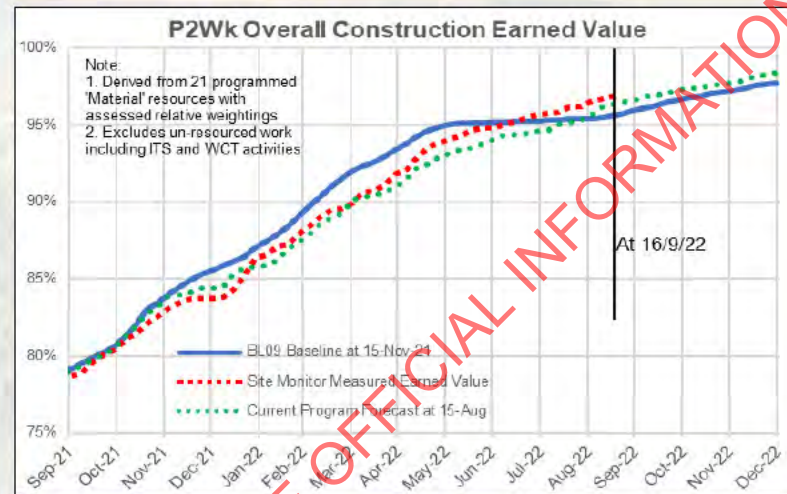

Key Progress & Notable Delays since 2nd September

- **Northern Roundabout traffic switch** completed 4th September.
- **AP65 being laid to MLRi link** connection
- **AC20 laid** on southbound lanes just north of Johnstones Hill tunnel and at Watsons Road bridge..
- Continuing **earthworks at WM5** and **Perry Rd access track**.
- **Pavement widening work to connect to existing SH1** north of northern roundabout.
- **Slip form barrier** work at Woodcocks Rd Bridge, Mahurangi Bridge and KEV Bridge
- Rock slope remediation at **CS16D** and **CN5**.
- **Slip remediation** earthworks at **Mahurangi access track** and **CN12**.

S	S	M	T	W	T	F
3 ☁️	4 ☁️	5 ☁️	6 ☁️	7 ☁️	8 ☁️	9 ☁️
10 ☀️	11 ☁️	12 ☁️	13 ☁️	14 ☁️	15 ☀️	16 ☁️












s 9(2)(j)

RELEASED UNDER THE OFFICIAL INFORMATION ACT 1982

DASHBOARD GRAPHS

Progress vs Programme Note: Baseline is BL09 of 15/11/21

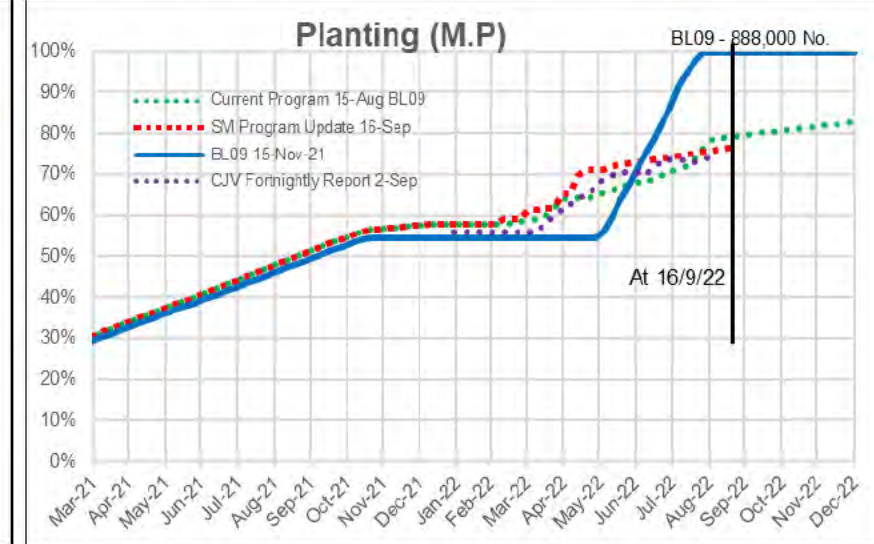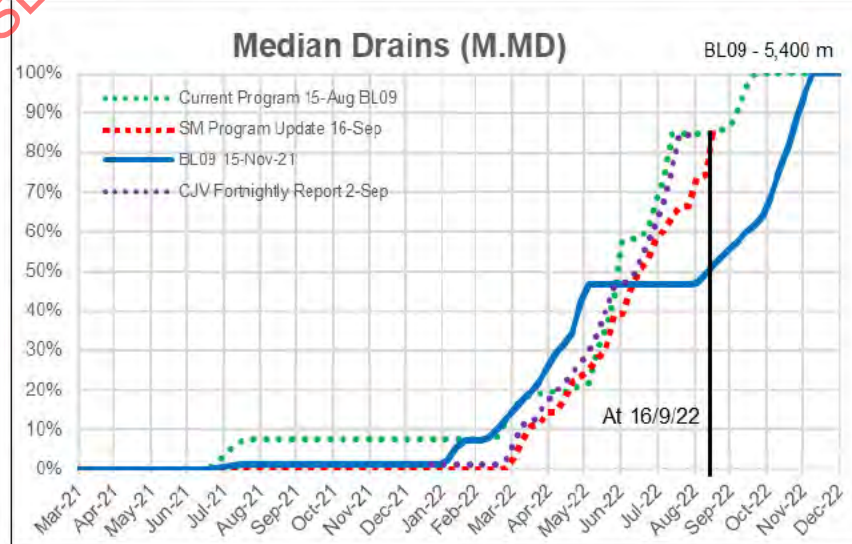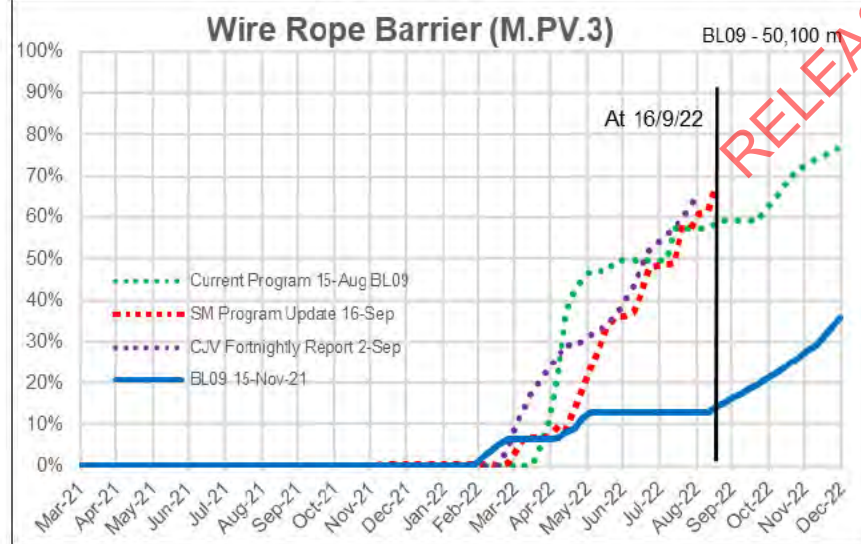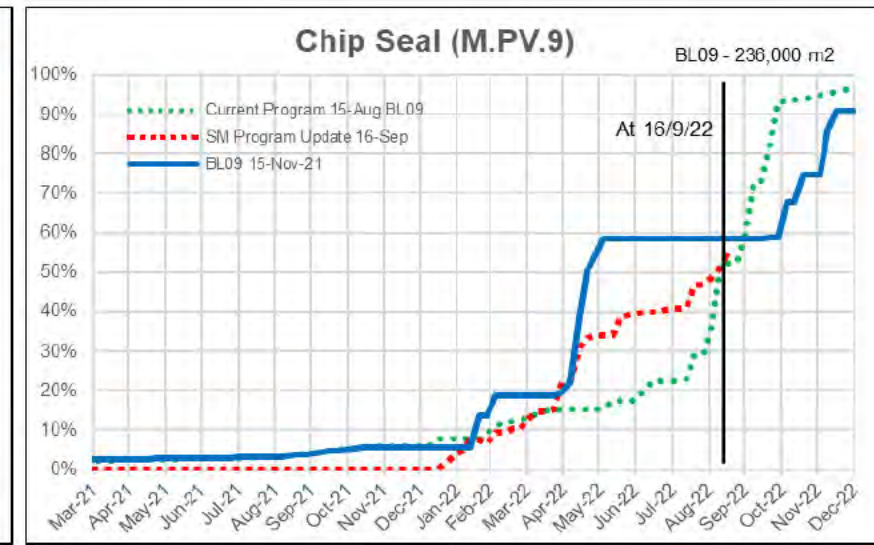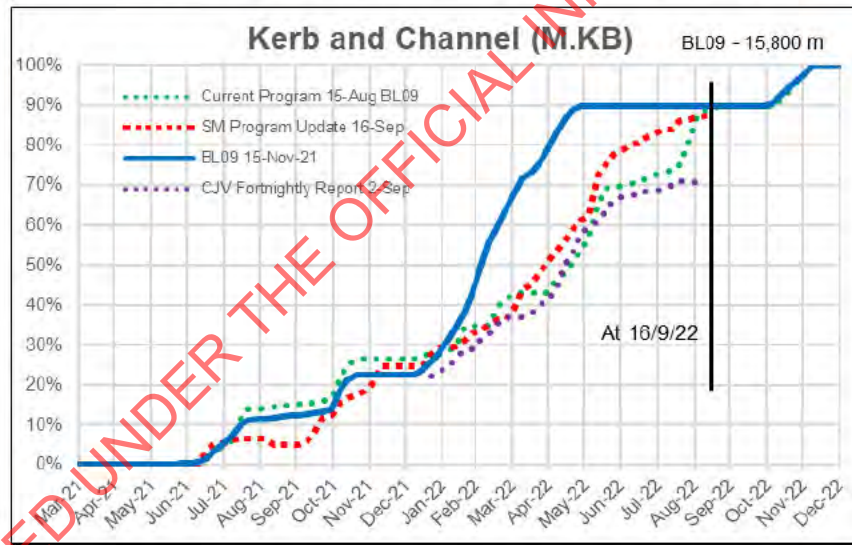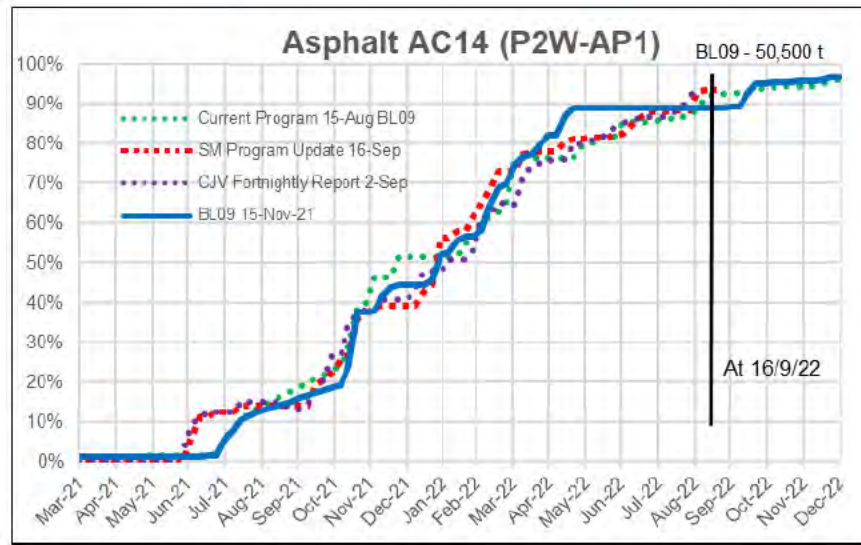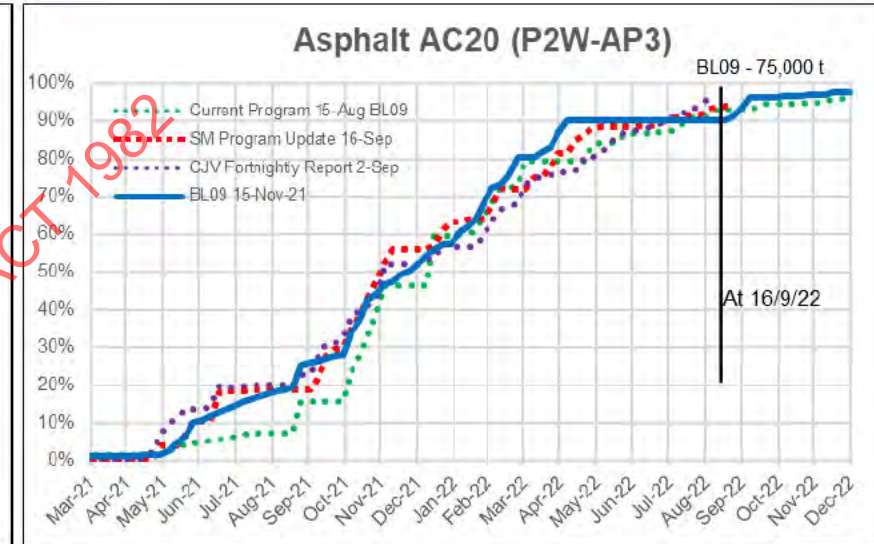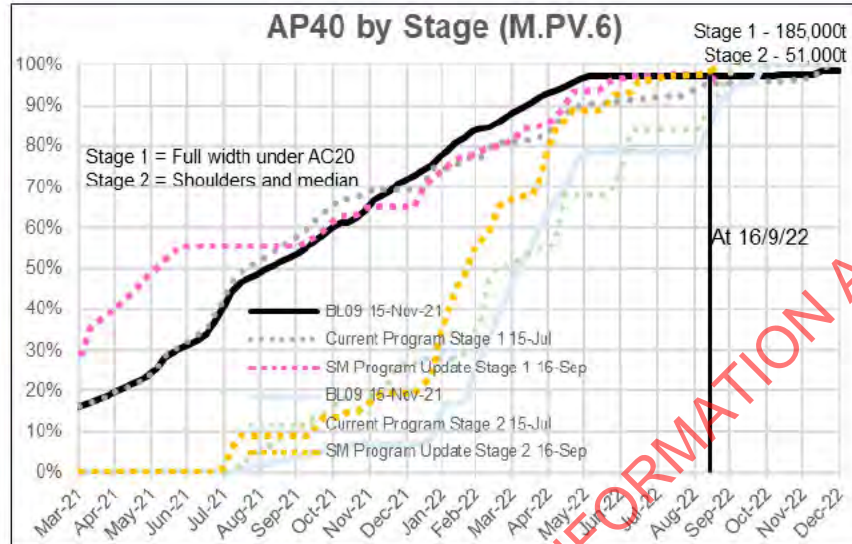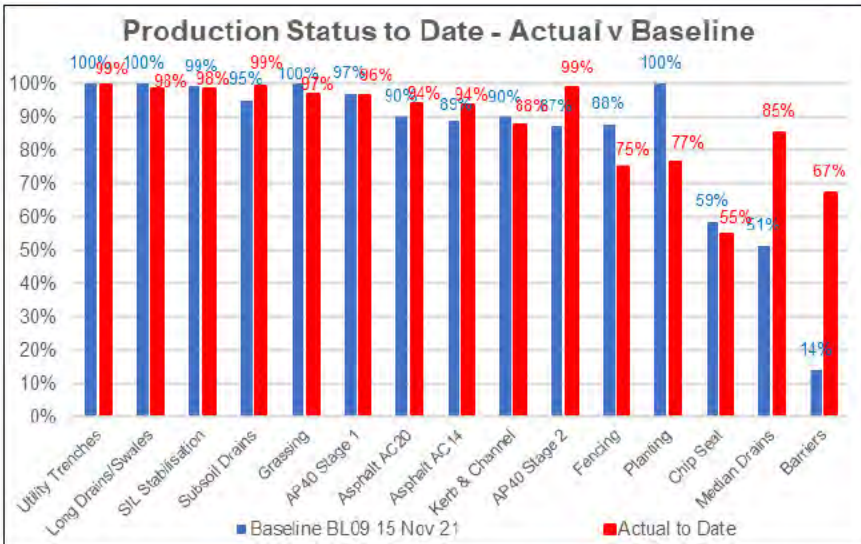

RELEASED UNDER THE OFFICIAL INFORMATION ACT 1982

RELEASED UNDER THE OFFICIAL INFORMATION ACT 1982

PROGRESS PHOTOS

15/09/22 Widening existing SH1, looking north



15/09/22 SH1 RAB Stage 3 TMP divert existing SH1 traffic onto alignment, looking north



16/09/22 WM5 earthworks, looking northeast



16/09/22 Perry Road access track earthworks, looking southwest



PROGRESS PHOTOS

15/09/22 CN12 slip remedial works, looking east



19/09/22 CS3 - Compacting AP40 Stage 2 on southbound shoulder, looking north



19/09/22 CS16D slip remedial works, looking north



19/09/22 S7 - Laying AC20 on southbound lanes, looking north



DASHBOARD

Plan showing P2Wk Alignment

