



TEMPORARY TRAFFIC LIGHT SAFETY

Please continue to stop for red lights at temporary traffic lights for your own safety, as well as that of other road users, and our work crews.

With repair work happening, you'll continue to see work sites and crews along State Highway 4.

Many of these sites have been reduced to a single lane, with temporary traffic lights controlling the flow of traffic. Roads are reduced to a single lane to help work crews perform repairs in a safe environment.



HAPOKOPOKO CURVE ROCK

We're happy with the progress being made on the Hapokopoko Rock Curve, north of Fields Track. We had a 2-week delay to works on the site last month due to the ground conditions, but work started up again on 25 September.

We also recently repaired the pavement in this section.

Despite the delay to work in September, we're still aiming to finish construction on the site by December this year.

Temporary traffic lights are operating on this site.



The SH4 bulletin will be available monthly at selected sites in Raetihi, Ohakune and Whanganui. We encourage you to read about progress on State Highway 4 (SH4) and share it with your whānau. If you have questions about anything you see in the SH4 bulletin there are a range of places to find out more on the back page.

SIGN UP to receive monthly updates online
nzta.govt.nz/sh4-repairs

TE OREORE UNDERSLIP

On the Te Oreore site, the pumps are running and doing a great job of keeping the ground water levels down. We're looking to install permanent electricity to the site soon, so the pumps can be operated from off-site.

This work supports reconstructing the permanent road, which we're hoping to get underway in the summer of 2021.

RAUKAWA

We're currently working through agreements and consent for this site and hope to begin physical work in the coming months.

WHISKEY CORNER

Work was completed on Whiskey Corner in June. This section has returned to normal operating speeds.

SOUTH RAUPIU RETREAT

Construction work is still on hold for this site due to an unstable slope face and wet weather conditions. Due to this delay and the necessary re-design, our expected completion date is now November/December this year.

Temporary traffic lights are operating on this site.

OTOKO PĀ OVERSLIP

All work on this site has been completed in May. The two slips that occurred in July continue to be monitored.


KUKUTA UNDERSLIP

The design work on this site is in its final stages. There are two historical sites outside the work area but close to the north end of this site. As there's the potential for further sites to be within the work area, an archaeologist has been engaged to undertake a more thorough assessment.

The site remains under one-way traffic lights.

SH4 CORRIDOR UPDATE

- 1 Te Oreore underslip:**
Work on permanent repair due to begin in 2021
- 2 Raukawa:**
Consent and agreement process
- 3 Hapokopoko Curve Rock:**
Estimated completion December 2020
- 4 Whiskey Corner:**
Completed
- 5 South Raupiu Retreat:**
Estimated completion Nov/Dec 2020
- 6 Otoko Pā overslip:**
Completed

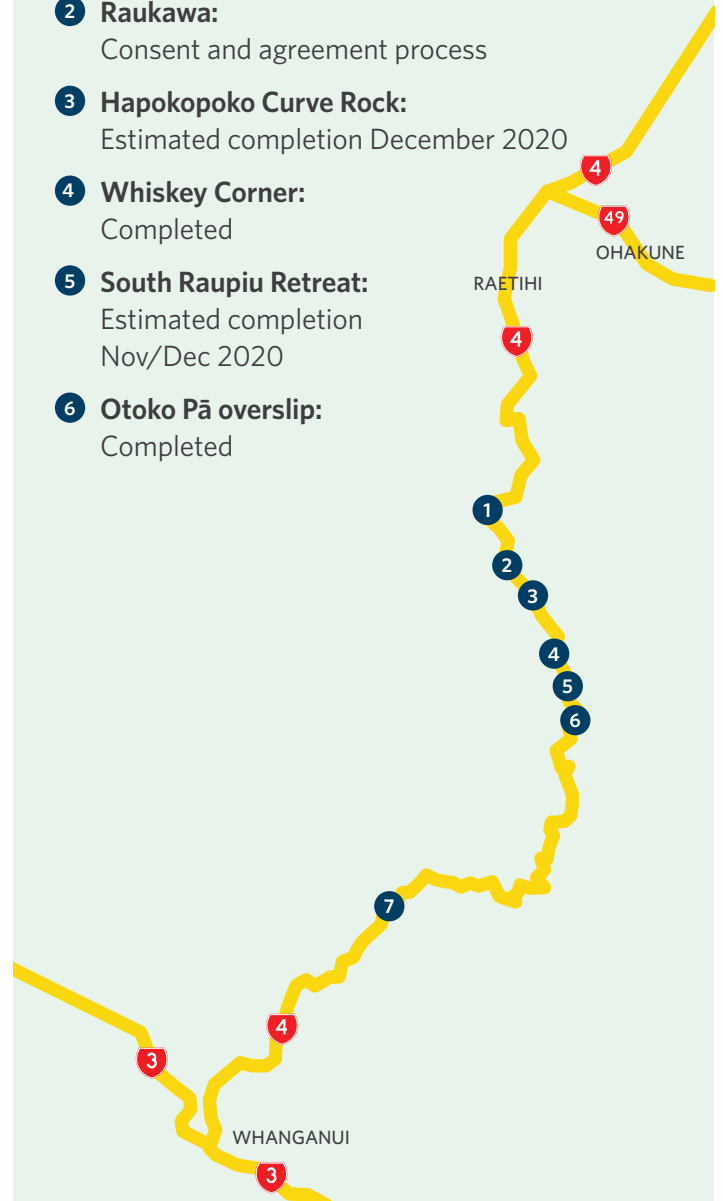

WHERE CAN WE GET COPIES OF SH4 BULLETIN?

Ruapehu District Council offices

Ohakune i-Site

Waiouru i-Site

Whakapapa Village i-Site

Ruapehu District Council - Main Office

Raetihi Caltex Motors

Raetihi Farm Supplies

Raetihi Four Square

Raetihi Information Centre

Ohakune BP Service Station

Ohakune New World

Placemakers Ohakune

GAS National Park

Whanganui District Council

Whanganui Library

Gonville Library

Z-Dublin St Service Station

Whanganui

BP 2Go Service Station

Whanganui

Whanganui i-Site

For more information and updates, please visit nzta.govt.nz/sh4-repairs

Traffic updates: nzta.govt.nz/traffic

Facebook: facebook.com/nztacni

Twitter: twitter.com/nztacni

Journey planner: journeys.nzta.govt.nz

Phone: **0800 4 HIGHWAYS** (0800 44 44 49)

If you have a smartphone, open the camera app and hover over the code to the right then click the link once prompted on your phone.

